

By: Shoumik, Moneba, Judy, Ekam & Abrar

Group Project: Team AB
FreshRoute Burndown.pdf

Team Members:


Name	Email	Student ID
Moneba Hanifi	moneba@my.yorku.ca	219721810
Shoumik Ahmed	shoumik@my.yorku.ca	219881598
Judy El Ghargomi	jelg21@my.yorku.ca	220227237
Ekambir Momi	ekam727@my.yorku.ca	219424407
Abrar Jawad Tarafder	abrart03@my.yorku.ca	219453497

3311 Section M Term W
Class Instructor: Ilir Dema
Sprint 2 Duration: March 10 - March 23, 2026


Fresh Route

Sprint Burndown Report

Burndown Chart Sprint 01

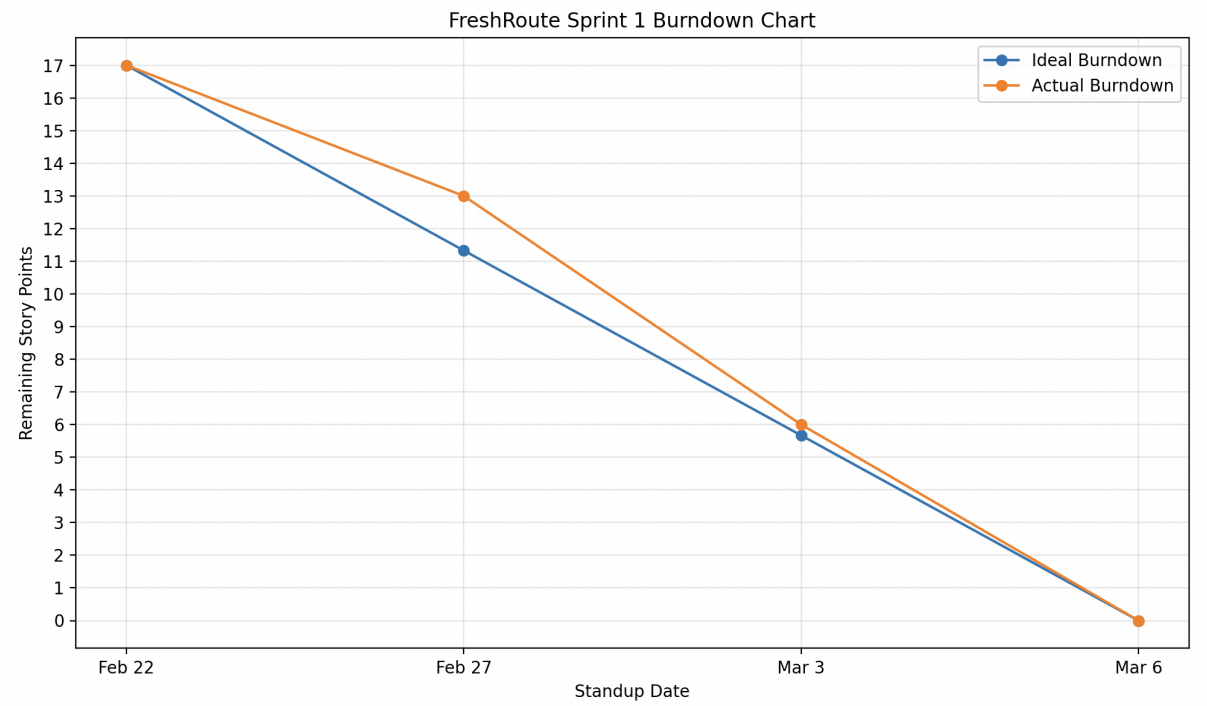

Burndown Chart Sprint 02

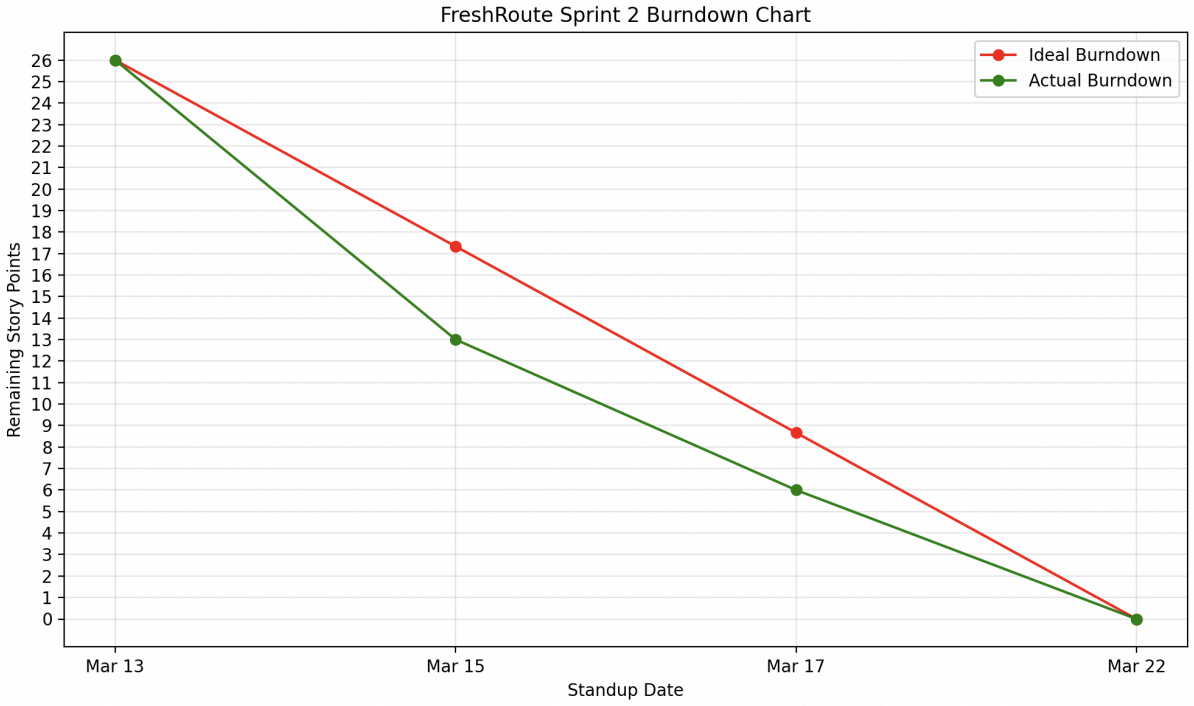

Burndown Chart Analysis

For Sprint 2, the team committed to 26 story points, which is an increase from Sprint 1, where the team committed to 17 story points. This represents an increase in the team's capacity and output. Early in Sprint 2, the actual burndown line drops faster than the ideal line, showing that a significant portion of the work was completed ahead of schedule. Most features were worked on continuously across multiple standups rather than being completed all at once. Because of this, progress was updated regularly, making the burndown chart a more accurate representation of when work was actually completed.

This pattern also aligns with the team's workload distribution for Sprint 2. A large portion of development occurred during the first week of Sprint 2, with over **30%** of commits made early in the sprint, as reflected in Trello. This early momentum helped the team get ahead of schedule and reduce risk for the remaining work.

As Sprint 2 progressed, the rate of completion became more aligned with the ideal burndown. This is because the remaining tasks, such as backend integration, cart persistence, and recipe-based functionality, were more complex and required additional coordination and testing, which were done with user stories and subtasks.

By the end of Sprint 2, the actual burndown reaches zero, meaning all committed story points were completed within the sprint timeframe. Overall, this shows that the team managed its workload effectively and maintained steady progress while handling a larger and more complex set of features. As a side note, Sprint 1 had also reached zero, so it is important to mention that no tasks from Sprint 1 were carried over as well.

Adequacy of Explanations and Match with Trello

The burndown chart closely matches the progress tracked on Trello. As tasks and user stories were completed, story points were consistently updated, and these updates are reflected directly in the chart.

Each drop in the burndown corresponds to completed work recorded on the Trello board, ensuring that the chart accurately represents the team's progress. Since tasks were actively worked on and updated throughout the standups, the chart reflects real development activity rather than delayed or bulk updates for the sprints.

This consistency between Trello and the burndown chart demonstrates strong tracking practices and provides a reliable, transparent view of the team's progress throughout the sprints.
