

By: Shoumik, Moneba, Judy, Ekam & Abrar

Group Project: Team AB
FreshRoute Burndown.pdf

Team Members:

Name	Email	Student ID
Moneba Hanifi	moneba@my.yorku.ca	219721810
Shoumik Ahmed	shoumik@my.yorku.ca	219881598
Judy El Ghargomi	jelg21@my.yorku.ca	220227237
Ekambir Momi	ekam727@my.yorku.ca	219424407
Abrar Jawad Tarafder	abrart03@my.yorku.ca	219453497


3311 Section M Term W

Class Instructor: Ilir Dema


Sprint 3 Duration: March 23 - April 06, 2026

Sprint Burndown Report


Burndown Chart Sprint 01

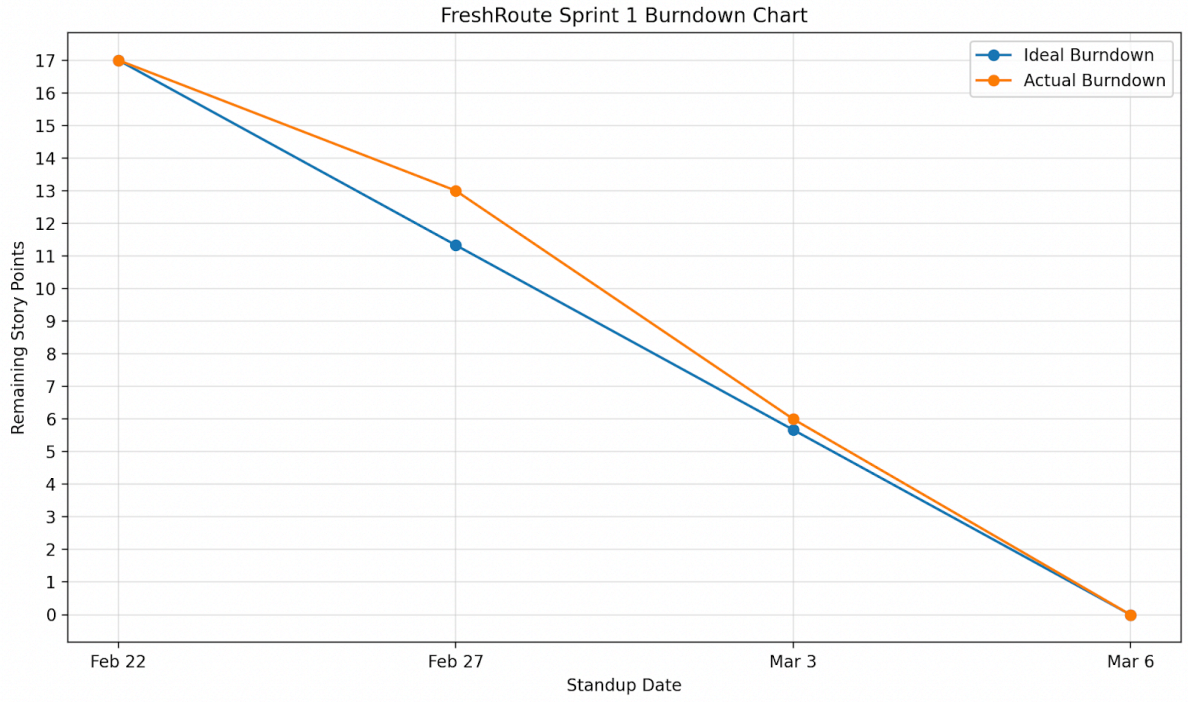

Burndown Chart Sprint 02

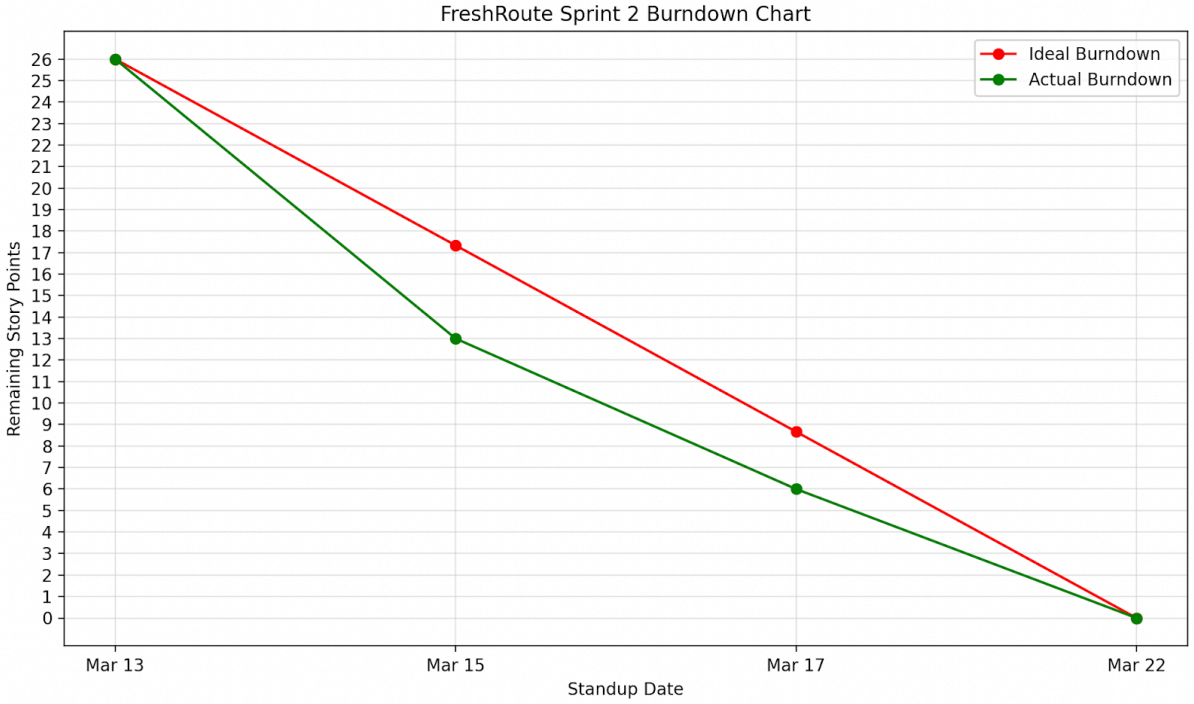

Burndown Chart Sprint 03

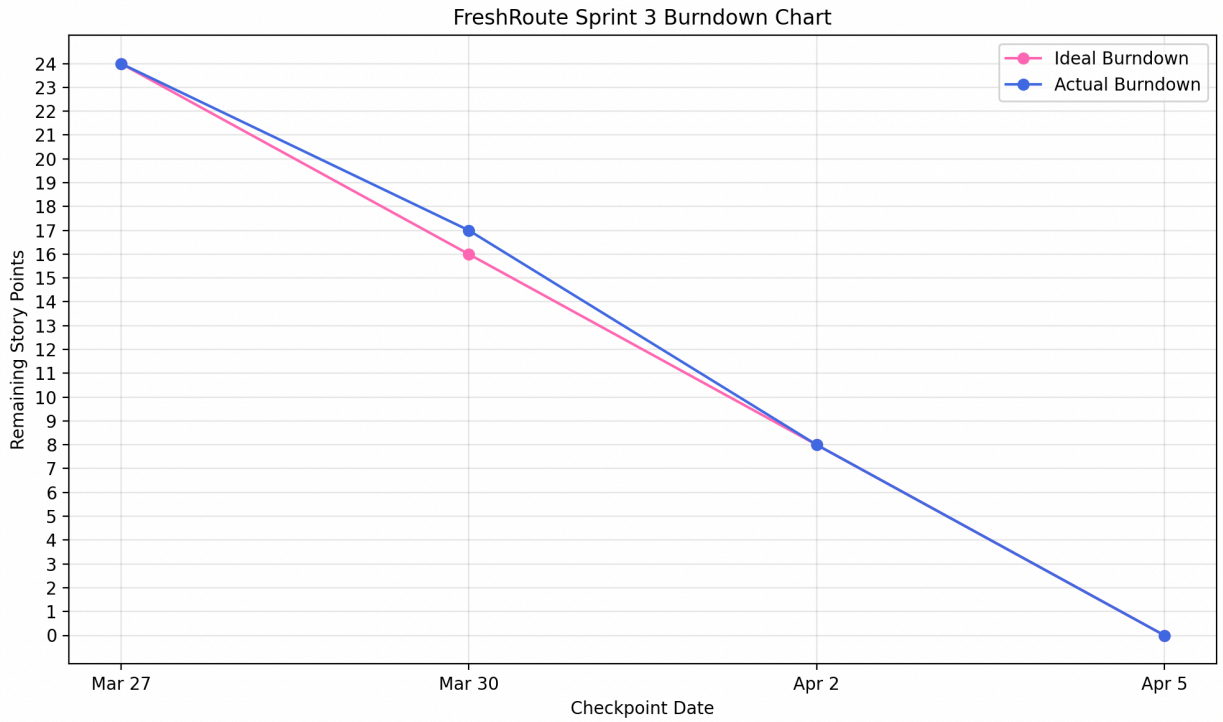

Burndown Chart Analysis

For Sprint 3, the team committed to 24 story points, an increase from Sprint 1 (17) and a very slight decrease from Sprint 2 (26). The overall story points represent an increase in the team's capacity and output from Sprint 1 to Sprint 2, and then maintaining that output / slightly less capacity, from Sprint 2 to Sprint 3, which is expected because Sprint 3 is more of a wrap-up sprint.

For Sprint 3, the burndown chart shows the team running ahead of the ideal line from the start. Between the first standup (Mar 27) and the second standup (Mar 30), the remaining points dropped from 24 to 17, reflecting very early delivery of the order flow foundations (checkout, order creation). At the second and third standups (Mar 30 - Apr 2), the line maintained a steady gap relative to the ideal line, as order confirmation, image integration subtasks, tracking, and cancel-order work continued in parallel, so progress remained continuous rather than spiky. The final checkpoint (Apr 5) hits zero, confirming all Sprint 3 commitments, including the new orders page with confirmation, backend image integration, order lookup, order connection to backend and cancellation, were all finished on time, with early momentum reducing risk for the later integration and testing steps.

This pattern also aligns with the team's workload distribution for Sprint 3. A very large portion of development occurred during the first week of Sprint 3, with over **30%** of

commits made very early in the sprint before week 1 had even finished, as reflected in Trello. This early momentum helped the team get ahead of schedule and reduce risk for the remaining work.

As Sprint 3 progressed, the rate of completion became more aligned with the ideal burndown, which was difficult, but we were able to achieve it. This is because the remaining tasks, such as backend image integration, the order confirmation page finalization, and order-tracking functionality finalization, were more complex and required additional coordination and testing, which were handled through user stories and subtasks.

By the end of Sprint 3, the actual burndown reaches zero, meaning all committed story points were completed within the sprint timeframe. Overall, this shows that the team managed its workload effectively and maintained steady progress while handling a larger and more complex set of features.

****As a side note, Sprint 1 and Sprint 2 had also reached zero, so it is important to note that no tasks from Sprint 1 and Sprint 2 were carried over. The fact that all three sprints were fully completed shows that the entire project was managed effectively among all team members.****

Adequacy of Explanations and Match with Trello

The burndown chart closely matches the progress tracked on Trello. As tasks and user stories were completed, story points were consistently updated, and these updates are reflected directly in the chart.

Each drop in the burndown corresponds to completed work recorded on the Trello board, ensuring that the chart accurately represents the team's progress. Since tasks were actively worked on and updated throughout the standups, the chart reflects real development activity rather than delayed or bulk updates for the sprints.

This consistency between Trello and the burndown chart demonstrates strong tracking practices and provides a reliable, transparent view of the team's progress throughout the sprints.
